

Whittier Tunnel Surface Improvements

Portage Glacier Road Whittier, AK | *** 99510



Date Sun 03/14/2021

Job # 119776

Prepared By Gabriel Thomas



Weather		
<p>3:00 AM</p> <p>5° </p> <p>Clear</p> <p>Wind: 4 MPH Precipitation: .0" Humidity: 71%</p>	<p>6:00 AM</p> <p>9° </p> <p>Mostly Cloudy</p> <p>Wind: 2 MPH Precipitation: .0" Humidity: 83%</p>	<p>10:00 PM</p> <p>22° </p> <p>Snow</p> <p>Wind: 3 MPH Precipitation: .11" Humidity: 94%</p>

Work Logs

Name	Description	Quantity	Total Hours	Total Hours To Date
ARRC Crew	<p>Ian Pierce - flagger - form B - r3434</p> <p>Gabriel Thomas - PM - R3612</p> <p>R3434 needs an oil change. Suggest take to anchorage in the AM and return in evening. Would like to do this when fuel tank is low to maximize fuel prices in anchorage.</p> <p>Gabriel Thomas 03/15/21 12:02AM</p>	2	17	17
Granite Crew	<p>Ripped asphalt on north rail (on safe house side of track) starting in front of, and north of safe house 8 and replaced with rubber flange filler.</p> <p>SH 8, two / three passes with loader bucket teeth mounts.</p> <p>38% of eclipse are broken on first 5 panels, less are broken track north of SH8</p> <p>13 panels of production. Starting 2 panels north of phone 582</p> <p>Slight damage to concrete in tubs. Need to keep an eye</p>	8	68	171.5

on it.

Rubber installation is smooth, no D clips, D clips will present a challenge for installation

Asphalt removal is damaging the joint seals, joint seals appear to be in bad shape to start with.

Granite has excavator on order

Gabriel Thomas | 03/15/21 | 12:22AM

Whittier Tunnel Inspection and Daily Reporting	0	0	0
Total	10	85	188.5

Time Cards

No entry

Materials

Material	Cost Code	Day Total	Week Total	Quantities to Date
Polycorp Field Rubber Flangeway One side of track Gabriel Thomas 03/15/21 03:53PM		97.5 lf	247.5 lf	247.5 lf
Polycorp Gauge Rubber Flangeway One side of track Gabriel Thomas 03/15/21 03:53PM		97.5 lf	247.5 lf	247.5 lf

Equipment

Equipment	Supplier/Sub	Hours In Use	Notes	Total Days On Site
Air Compressor - Sullair A765-05 Granite		0		1

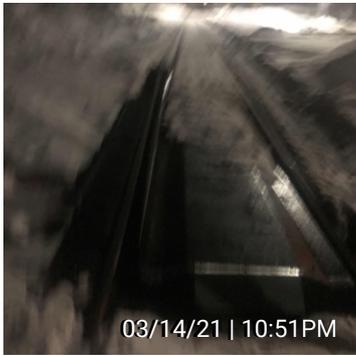
General Notes

1. 2140 SB Whittier freight confirmed south of tunnel portal

Gabriel Thomas | 03/14/21 | 09:47PM

2. Switch freezing causing delay Friday

Gabriel Thomas | 03/14/21 | 11:20PM



3. Need to get Dispatch to notify Arcc flagger when train is totally south of girwood detector. Train is about 40 min travel from this detector to the Whittier tunnel.
Gabriel Thomas | 03/15/21 | 04:53AM
4. In the past the portage tunnel was left open over night by section to prevent Tom from having to man the portage doors. Confirm that flagger can man doors while on form B
Gabriel Thomas | 03/15/21 | 04:54AM
5. Need to confirm weekend hours with tunnel control and granite
Gabriel Thomas | 03/15/21 | 04:55AM

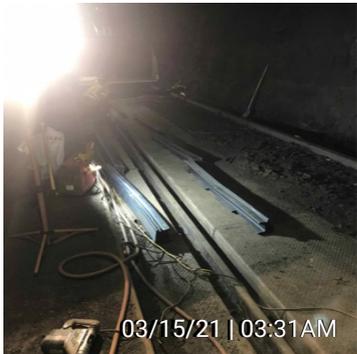
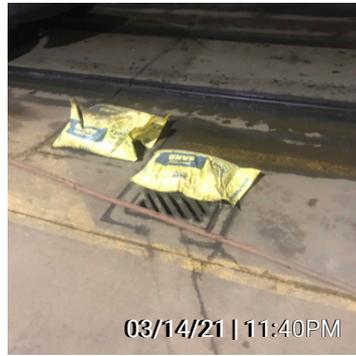
Site Safety Observations No entry

Quality Control Observations No entry

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	Safety meeting held at 10:30 PM Gabriel Thomas 03/15/21 12:43AM
2. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	No trains Gabriel Thomas 03/15/21 12:43AM
3. Did weather cause any delays?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	Stormy in Whittier Gabriel Thomas 03/15/21 12:43AM
4. Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	No Gabriel Thomas 03/15/21 12:43AM
5. Any areas that can't be worked on?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6. Any equipment rented on site?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	

Attachments

A handwritten signature in black ink, appearing to be "GOT".

I, Gabriel Thomas, have reviewed and completed this report.

Gabriel Thomas | 03/15/21 | 06:24AM
